

Client:	Needham DPW	Dates:	03/04/2017 to 03/10/2017
Contract:	Downtown Improvements		
Contractor:	MDR Construction Co., Inc.	Inspector on site:	P.C.

WORK COMPLETED THIS WEEK

- Completed installation of the mast arms and signal heads
- Continued installation of the pedestrian signals and posts
- Continued installing the new wiring for traffic signal components and street lights in various locations
- Installed the conduit from Great Plain Ave to the MBTA controller hand hole along the tracks


WORK ANTICIPATED FOR NEXT WEEK

- All work scheduled to take place during the day and is weather dependent
- Begin installation of light poles and continue the installation of the bollards
- Continue installation of wiring for various electrical/traffic signal components
- Connect new conduit to the existing electrical vaults in Great Plain Ave. at Chapel St. and Highland Ave. (not completed last week and dependent on Eversource scheduling the work)
- Construct the foundations for future kiosk, statue and fountain (not completed last week)
- Continue shop drawing submissions and processing

PHOTOS



Installing the mast arm pole just west of the train tracks in Great Plain Ave.

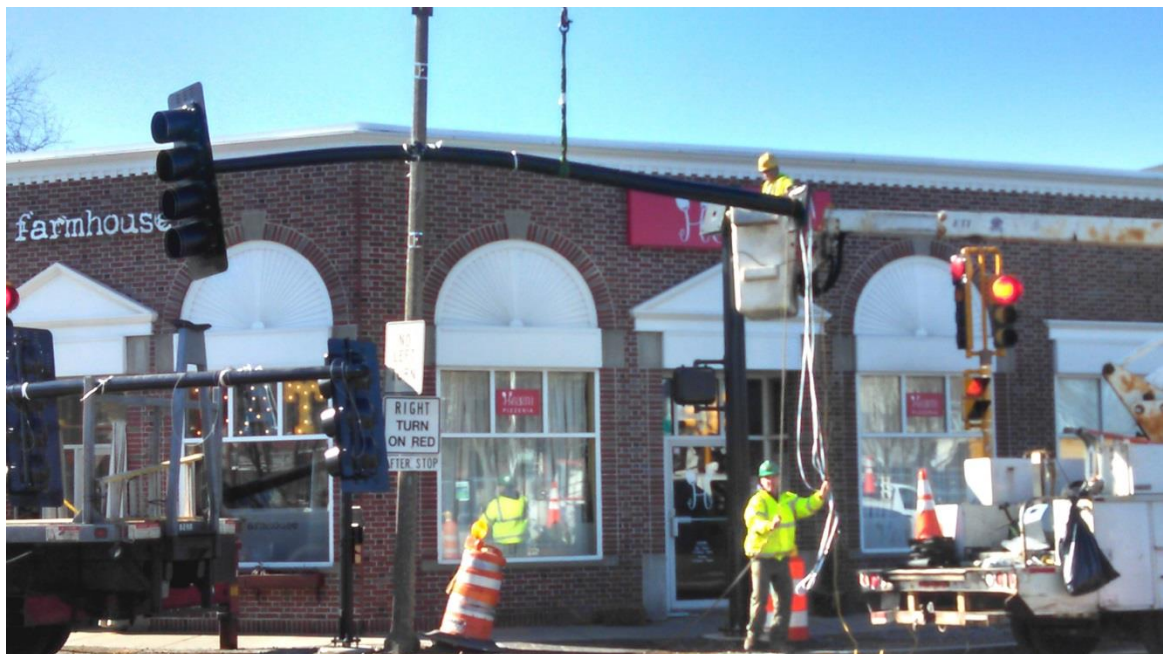

Installing the mast arm on the southwest corner of Great Plain Ave. and Dedham Ave.



Mast arms being prepped for installation in front of the Common




Traffic signal equipment being stored at the staging area



Excavating for installation of 3 inch schedule 80 PVC conduit in MBTA right-of-way with Keolis flagman to the left



Trench for 3 inch PVC schedule 80 conduit showing sand bedding, warning tape and existing cables near sidewalk

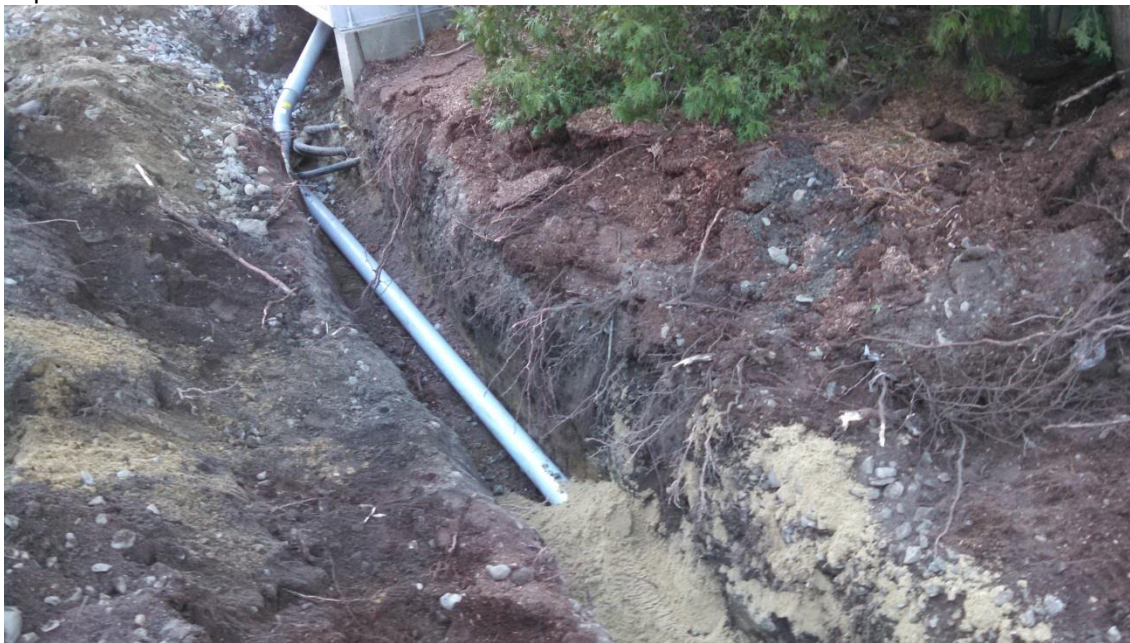

3 inch schedule 80 PVC conduit being installed to existing controller in MBTA property
also showing existing cables near controller
