




Data Date: 14-Apr-18  
Project Start: 17-Apr-18  
Project Finish: 03-Sep-19

UNDERGROUND

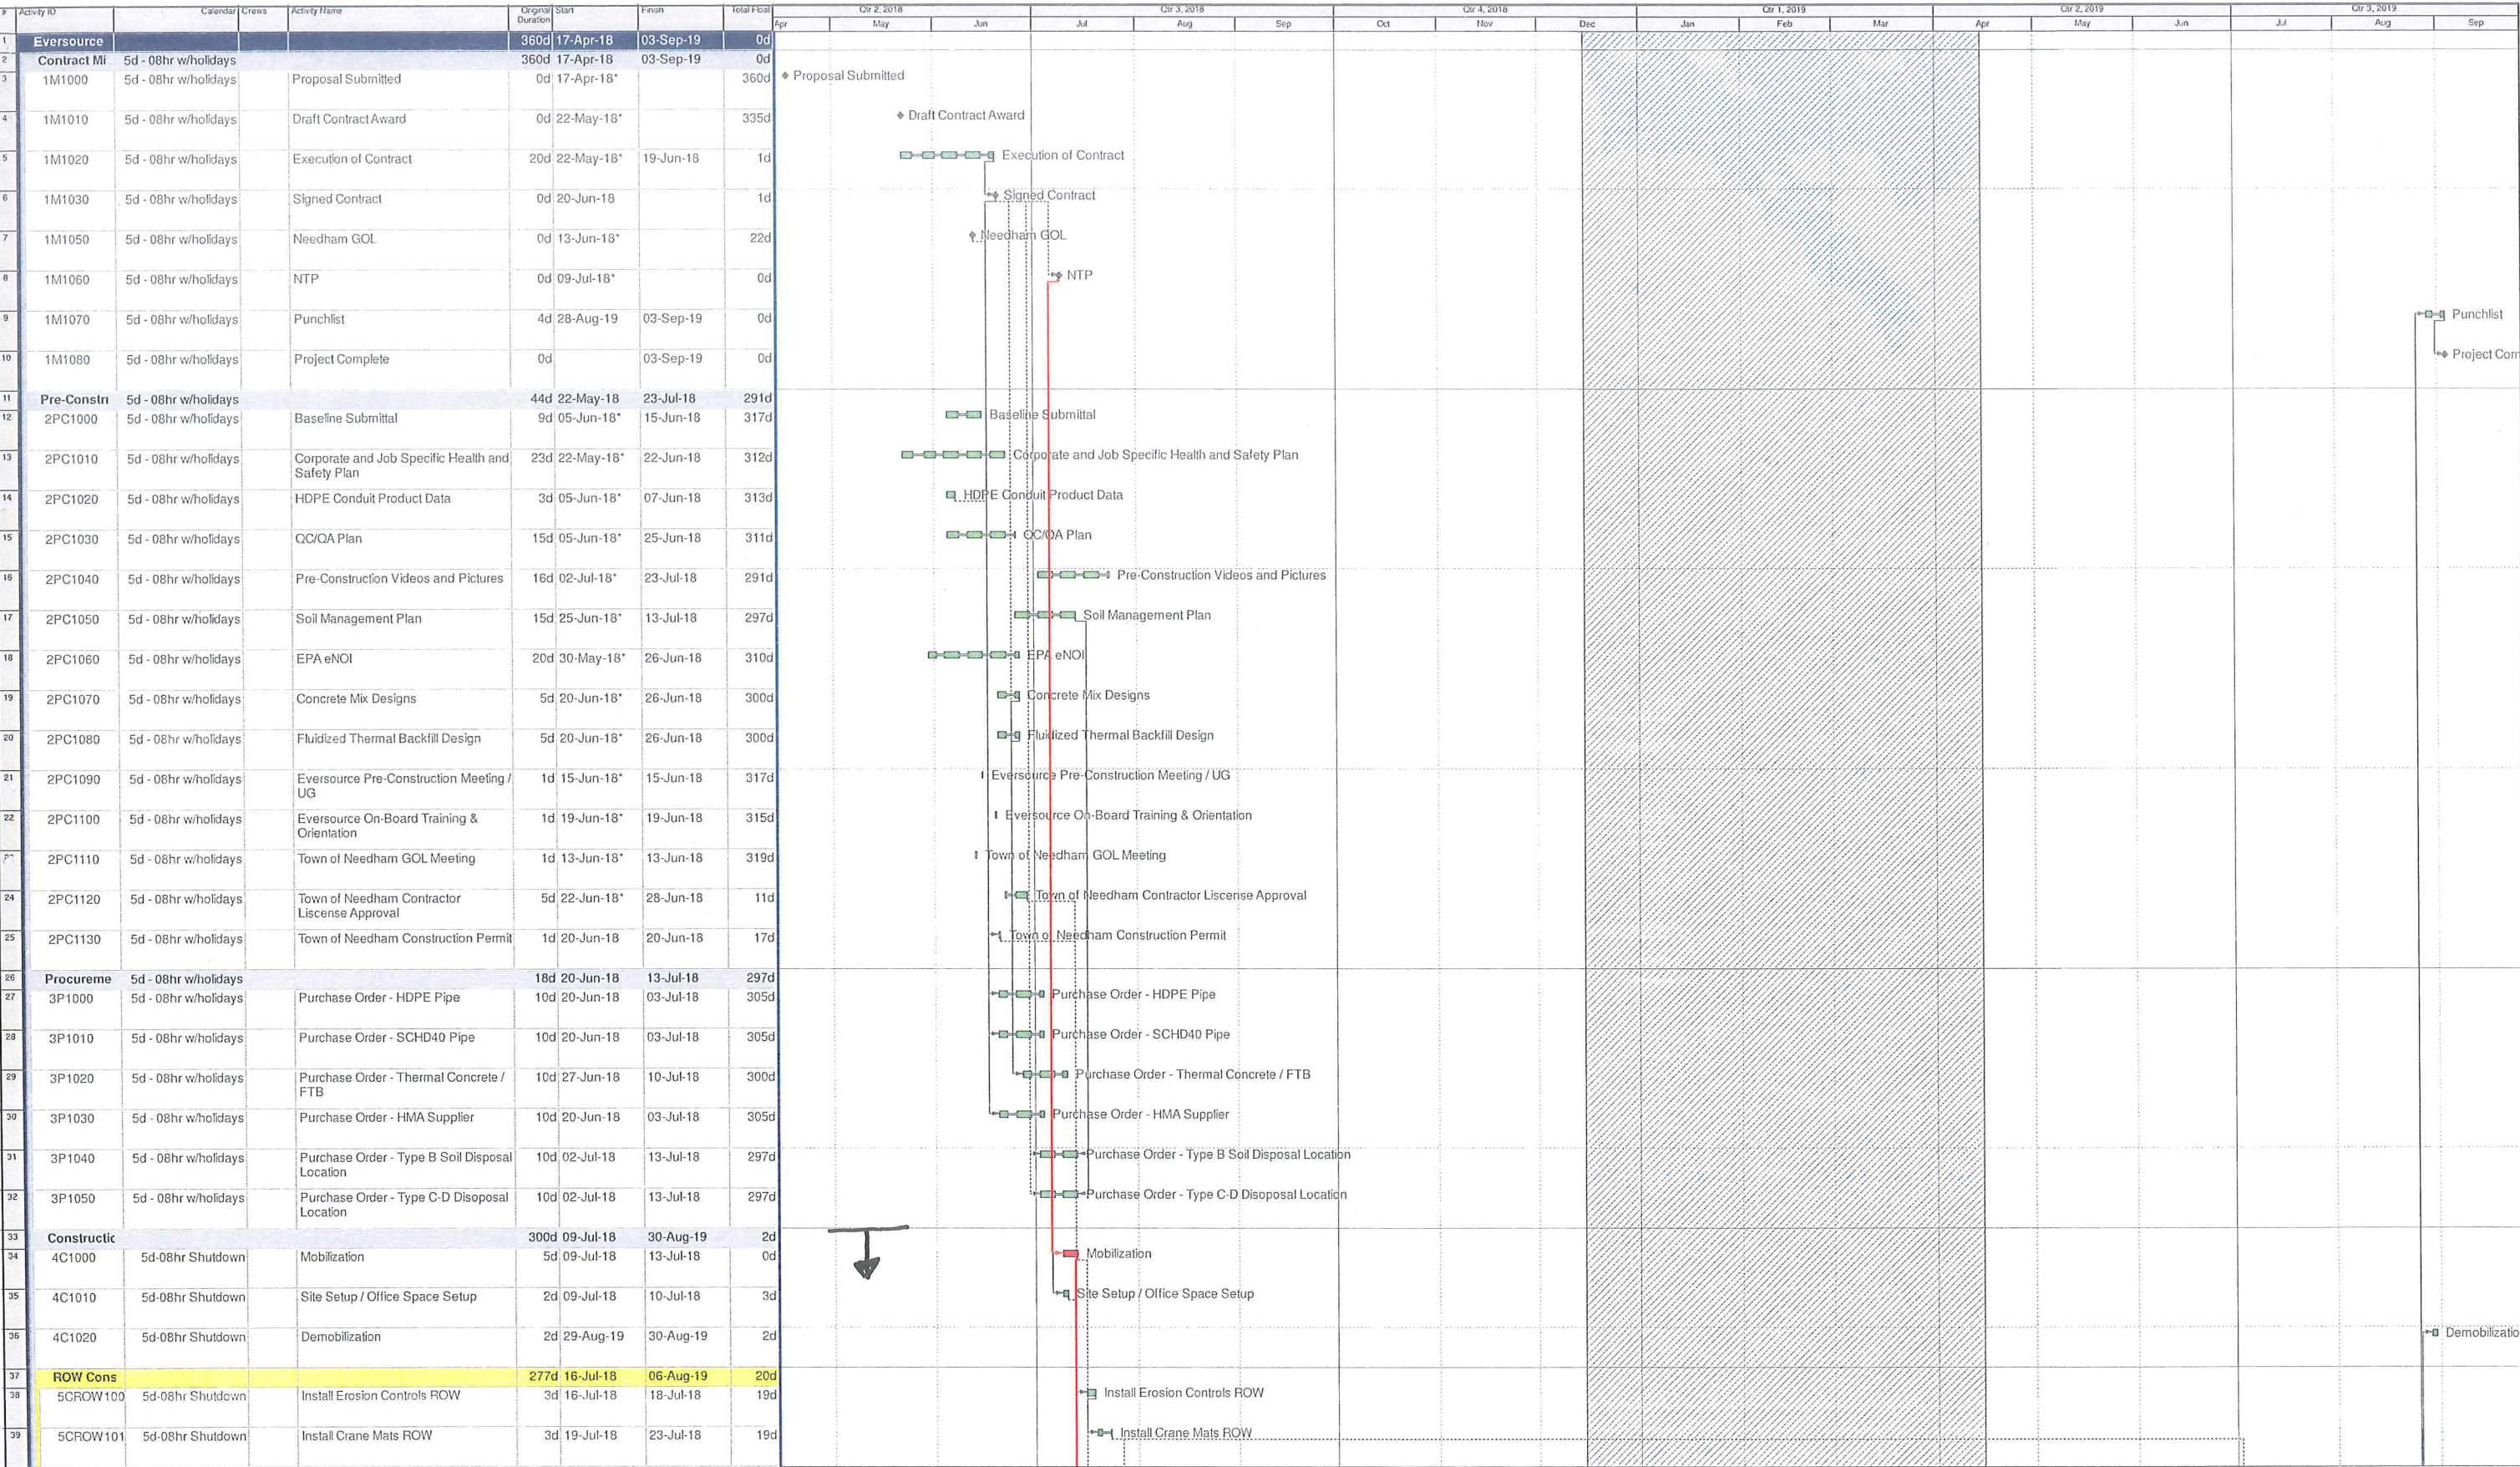

| #  | Activity ID | Calendar             | Crews  | Activity Name                                                  | Original Duration | Start Date | Finish Date | Total Hours |
|----|-------------|----------------------|--------|----------------------------------------------------------------|-------------------|------------|-------------|-------------|
| 40 | 5CROW102    | 5d - 08hr w/holidays | Crew B | Build Riser Struction STA 0+00                                 | 5d                | 05-Jul-19* | 12-Jul-19   | 37d         |
| 41 | 5CROW103    | 5d - 08hr w/holidays | Crew D | Install 115kV Transmission Line Duct Bank STA 0+00 to 11+50    | 194d              | 18-Jul-18* | 15-Apr-19   | 20d         |
| 42 | 5CROW104    | 5d-08hr Shutdown     |        | ROW Restoration & Seeding                                      | 3d                | 16-Apr-19  | 18-Apr-19   | 98d         |
| 43 | 5CROW105    | 5d-08hr Shutdown     | Crew D | Build Riser Structure Sta. 152+44                              | 5d                | 31-Jul-19  | 06-Aug-19   | 20d         |
| 44 | Roadway C   | 5d-08hr Shutdown     |        |                                                                | 207d              | 16-Jul-18  | 28-Aug-19   | 4d          |
| 45 | 6RW1000     | 5d-08hr Shutdown     | Crew A | Install 115kV Transmission Line Duct Bank STA 152+44 to 134+65 | 72d               | 16-Jul-18  | 23-Oct-18   | 0d          |
| 46 | 6RW1002     | 5d-08hr Shutdown     | Crew B | Install 115kV Transmission Line Duct Bank STA 11+50 to 23+75   | 49d               | 08-Aug-18  | 15-Oct-18   | 37d         |
| 47 | 6RW1003     | 5d-08hr Shutdown     | Crew B | Install 115kV Transmission Line Duct Bank STA 23+75 to 31+40   | 31d               | 16-Oct-18  | 27-Nov-18   | 37d         |
| 48 | 6RW1010     | 5d-08hr Shutdown     | Crew C | Install 115kV Transmission Line Duct Bank STA 134+65 to 116+54 | 72d               | 16-Oct-18  | 23-May-19   | 15d         |
| 49 | 6RW1011     | 5d-08hr Shutdown     | Crew A | Install 115kV Transmission Line Duct Bank STA 116+54 to 100+35 | 65d               | 24-Oct-18  | 22-May-19   | 0d          |
| 50 | 6RW1012     | 5d-08hr Shutdown     | Crew B | Install 115kV Transmission Line Duct Bank STA 31+40 to 49+29   | 72d               | 28-Nov-18  | 05-Jul-19   | 37d         |
| 51 | 6RW1013     | 5d-08hr Shutdown     | Crew D | Install 115kV Transmission Line Duct Bank STA 68+27 to 49+29   | 76d               | 16-Apr-19* | 30-Jul-19   | 20d         |
| 52 | 6RW1030     | 5d-08hr Shutdown     | Crew A | Install 115kV Transmission Line Duct Bank STA 100+35 to 82+85  | 70d               | 23-May-19  | 28-Aug-19   | 0d          |
| 53 | 6RW1040     | 5d-08hr Shutdown     | Crew C | Install 115kV Transmission Line Duct Bank STA 82+85 to 68+27   | 58d               | 24-May-19  | 13-Aug-19   | 15d         |
| 54 | Manhole C   | 5d-08hr Shutdown     |        |                                                                | 66d               | 16-Jul-18  | 15-Oct-18   | 15d         |
| 55 | 7CM1000     | 5d-08hr Shutdown     | Crew C | Test Pit MH 3-8                                                | 3d                | 16-Jul-18  | 18-Jul-18   | 15d         |
| 56 | 7CM1005     | 5d-08hr Shutdown     | Crew C | Install MH No. 9 STA 134+65                                    | 7d                | 19-Jul-18  | 27-Jul-18   | 15d         |
| 57 | 7CM1015     | 5d-08hr Shutdown     | Crew C | Install MH No.1 STA 10+77                                      | 7d                | 30-Jul-18  | 07-Aug-18   | 15d         |
| 58 | 7CM1025     | 5d-08hr Shutdown     | Crew C | Install MH No.2 STA 23+75                                      | 7d                | 08-Aug-18  | 16-Aug-18   | 15d         |
| 59 | 7CM1035     | 5d-08hr Shutdown     | Crew C | Install MH No.3 STA 31+40                                      | 7d                | 17-Aug-18  | 27-Aug-18   | 15d         |
| 60 | 7CM1045     | 5d-08hr Shutdown     | Crew C | Install MH No.4 STA 49+29                                      | 7d                | 28-Aug-18  | 05-Sep-18   | 15d         |
| 61 | 7CM1055     | 5d-08hr Shutdown     | Crew C | Install MH No.5 STA 68+27                                      | 7d                | 06-Sep-18  | 14-Sep-18   | 15d         |
| 62 | 7CM1065     | 5d-08hr Shutdown     | Crew C | Install MH No.6 STA 82+85                                      | 7d                | 17-Sep-18  | 25-Sep-18   | 15d         |
| 63 | 7CM1075     | 5d-08hr Shutdown     | Crew C | Install MH No.7 STA 100+35                                     | 7d                | 26-Sep-18  | 04-Oct-18   | 15d         |
| 64 | 7CM1085     | 5d-08hr Shutdown     | Crew C | Install MH No.8 STA 116+54                                     | 7d                | 05-Oct-18  | 15-Oct-18   | 15d         |

Data Date: 14-Apr-18  
Project Start: 17-Apr-18  
Project Finish: 03-Sep-19

The Middlesex Corporation  
Eversource Needham Project Schedule  
Page 2 of 2

