

Client:	Needham DPW	Dates:	04/22/2017 to 04/28/2017
Contract:	Downtown Improvements		
Contractor:	MDR Construction Co., Inc.	Inspector on site:	D.K.

WORK COMPLETED THIS WEEK

- Completed installation of the fiber optic cable to the Town Hall IT server room
- Continued connecting the wiring of the luminaires to the lighted bollards and street lights
- Continuing to modify traffic signal settings and cycles as required
- Completed construction of the brick masonry wall on the west side of the Common and began construction of the brick masonry wall on the east side of the Common
- Installed the concrete foundation, flagpole sleeve, and up lighting conduit for the new flagpole in the Common
- Installed the concrete foundation for the future kiosk on the west side of the Common
- Began installation of the banner arms on the light poles

WORK ANTICIPATED FOR NEXT WEEK

- All work scheduled to take place during the day
- Continue connecting the wiring of the luminaires to the lighted bollards
- Install the concrete foundations for the future statue on the east side of the Common and the concrete foundation for the future fountain or historic statue in the Dedham Ave. island
- Complete the construction of the brick masonry wall at the east side entrance to the Common
- Begin setting some of the granite seat walls in the Common
- Continue to modify traffic signal settings and cycles as required
- Begin installation of the structural soil associated with the future tree plantings in sidewalk areas (not begun to date)
- Continue shop drawing submissions and processing

PHOTOS



Excavation for the new flagpole foundation




Sleeve and base plate for new flagpole being installed



Rear of brick masonry wall completed on the west side Common entrance



Continued construction of the brick masonry wall on the east side of the Common entrance

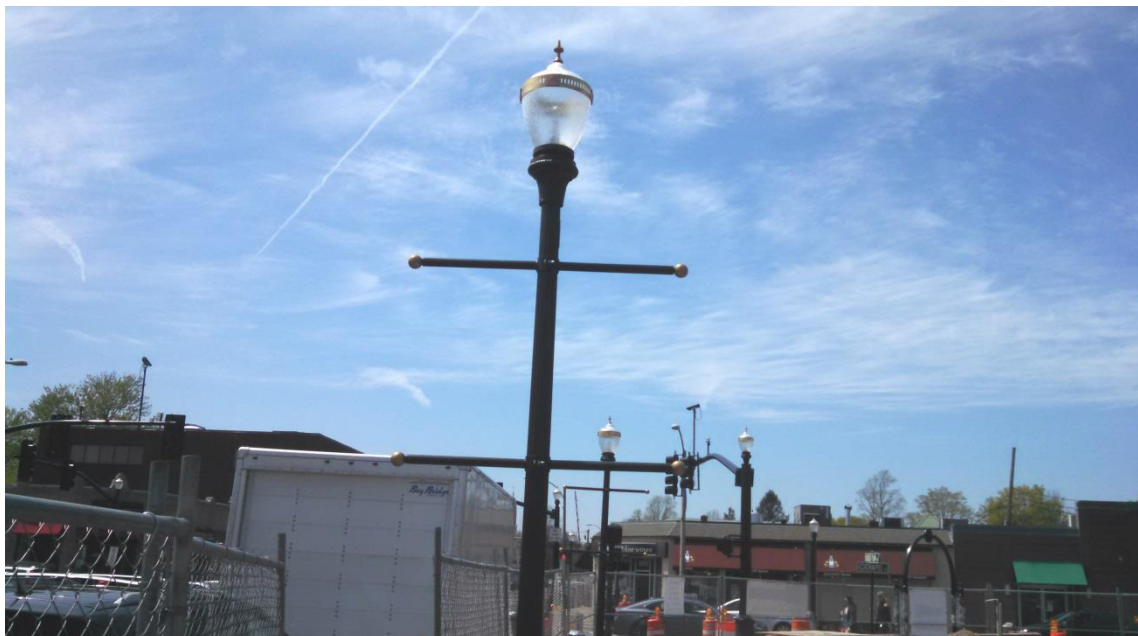

New banner arms installed on the new street lights



New granite seat wall, pavers and capstones ready for installation
