

WEEKLY SUMMARY REPORT

Client: Needham DPW Dates: 06/17/2017 to 06/23/2017

Contract: Downtown Improvements

Contractor: MDR Construction Co., Inc. Inspector on site: P.C.

WORK COMPLETED THIS WEEK

- Work is taking place both during the day and overnight with two separate crews
- Continuing to modify traffic signal settings and cycles as required
- Completed the installation of the granite and brick pavers in the Dedham Ave. Island
- Completed installation of the structural fill (for tree installation) in all required locations
- Continued installation of the granite planters with wood seats on the southeast corner of Great Plain Ave. and Dedham Ave. and the northeast corner of Great Plain Ave. and Highland Ave.
- Continued excavation of existing concrete sidewalk and installation of new concrete sidewalk
- Began installation of brick paver sidewalk strip
- Began installation of tree grates

WORK ANTICIPATED FOR NEXT WEEK

- Work is scheduled to continue to be performed during the day and overnight by two separate crews including this Saturday night and Sunday during the day in order to accommodate businesses in the placement of concrete sidewalks
- Begin installation of concrete brick pavers in the Dedham Ave. island crosswalk
- Continue with the installation of concrete sidewalks in various locations
- Continue installation of tree grates
- Complete the installation of sidewalk granite planters with wood seat
- Continue to modify traffic signal settings and cycles as required
- Continue with excavation and installation of new pavement in street locations where required
- Remove the old street lighting posts
- Finalize plans for the beginning of the brick paver crosswalk installation



Dedham Ave. island with granite and brick pavers installed




Placing concrete sidewalk in Highland Ave. in front of Santander Bank





New concrete sidewalk in Dedham Ave. west showing brick paver strip and tree grate

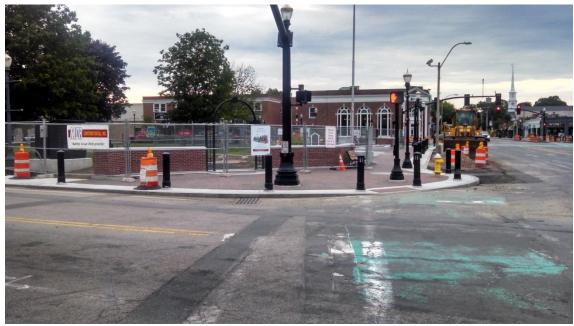

Front of Common looking west to east about 90% complete

